




# SCSH North Channel Flood Control Project Update July 25, 2022

Christopher Stevens, Chair  
Ad Hoc Committee  
North Indio Stormwater Flood Control  
Project

# North Indio Flood Hazards

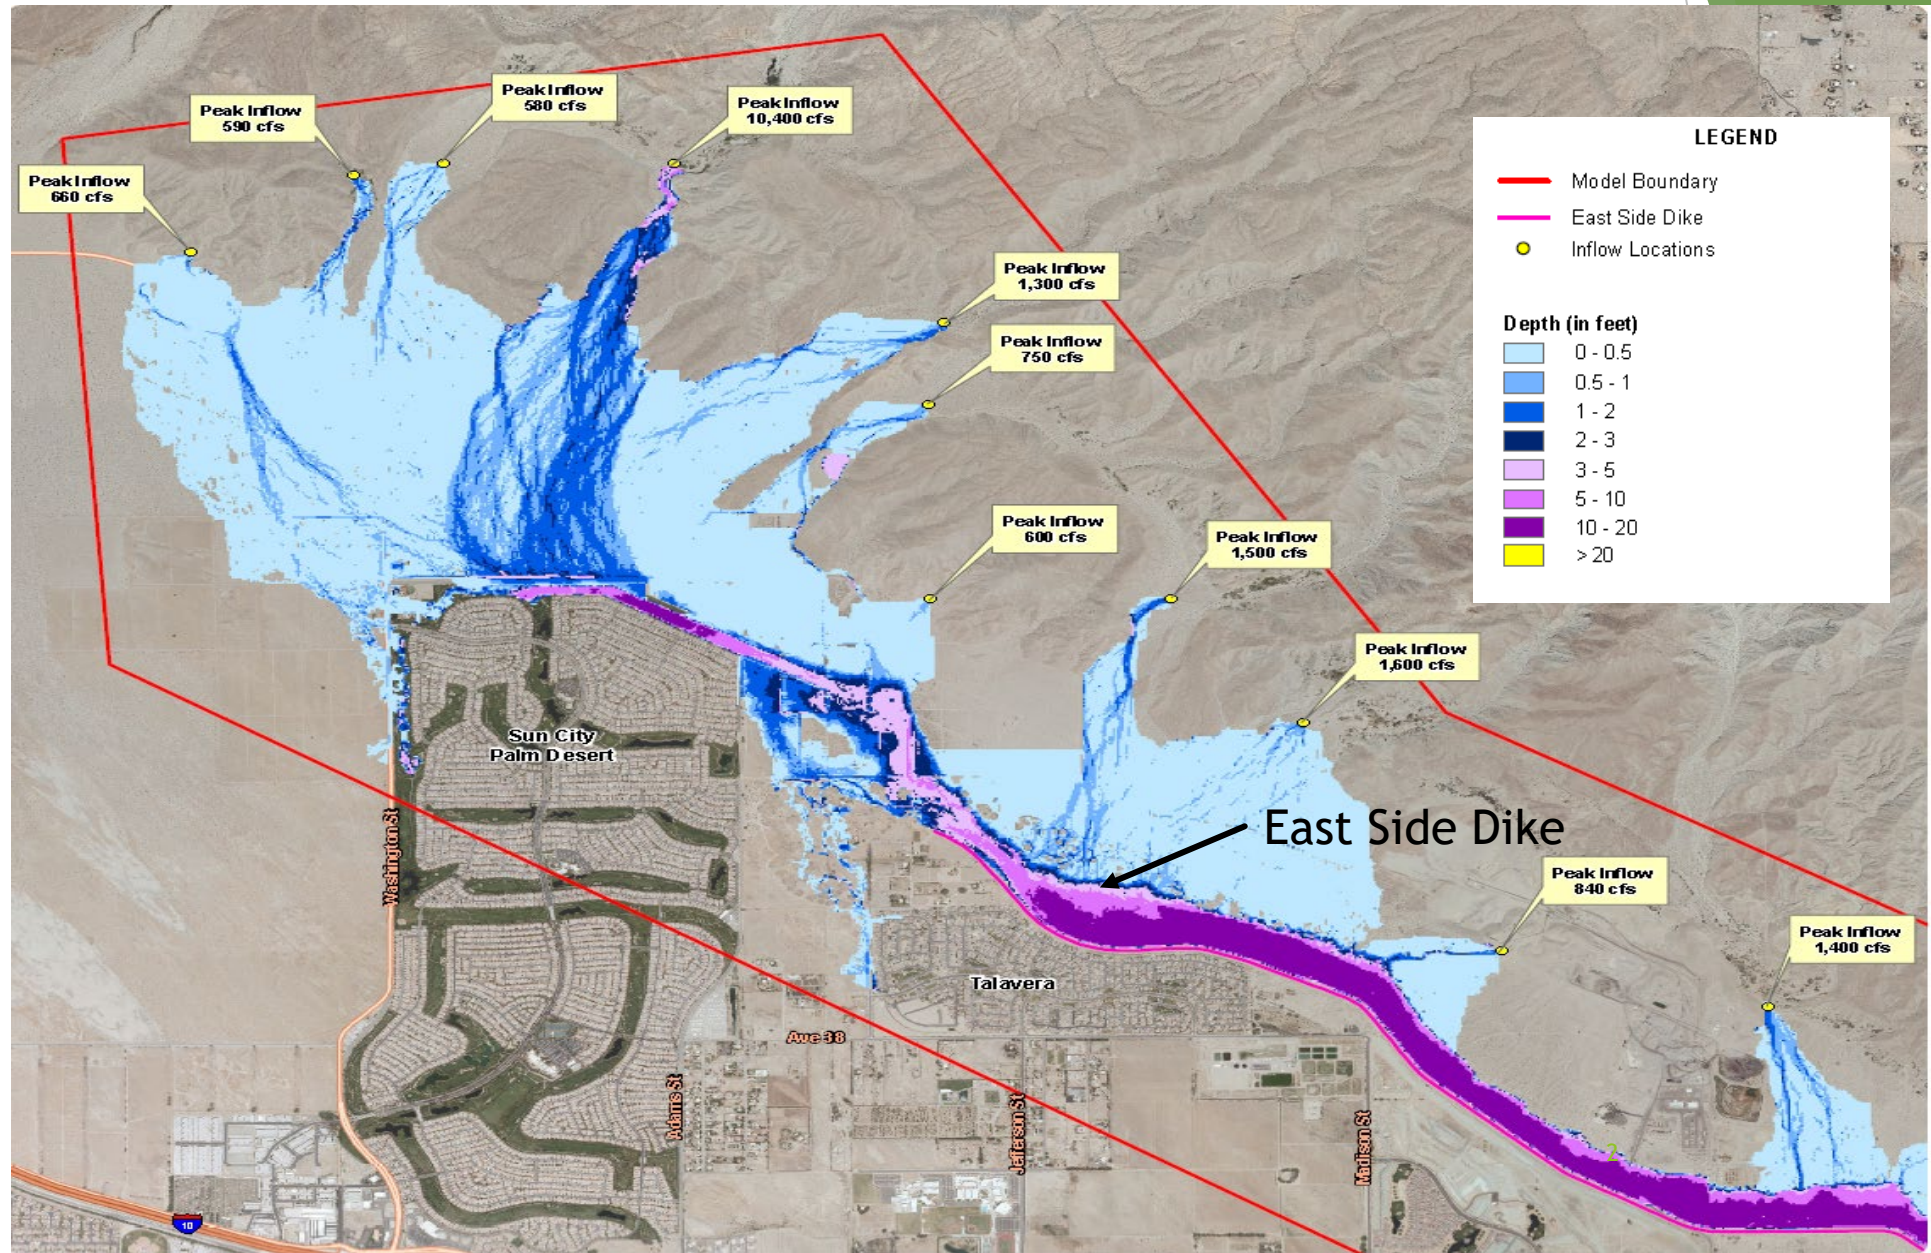

Data Sources: NAIP Orthorectified Color Aerial Imagery, 2010. County of Riverside Roads, 01/2014.



# North Connection Existing Channel Impacts






# North Connection Existing Channel Impacts





# SCSH Flood Control Project Overview

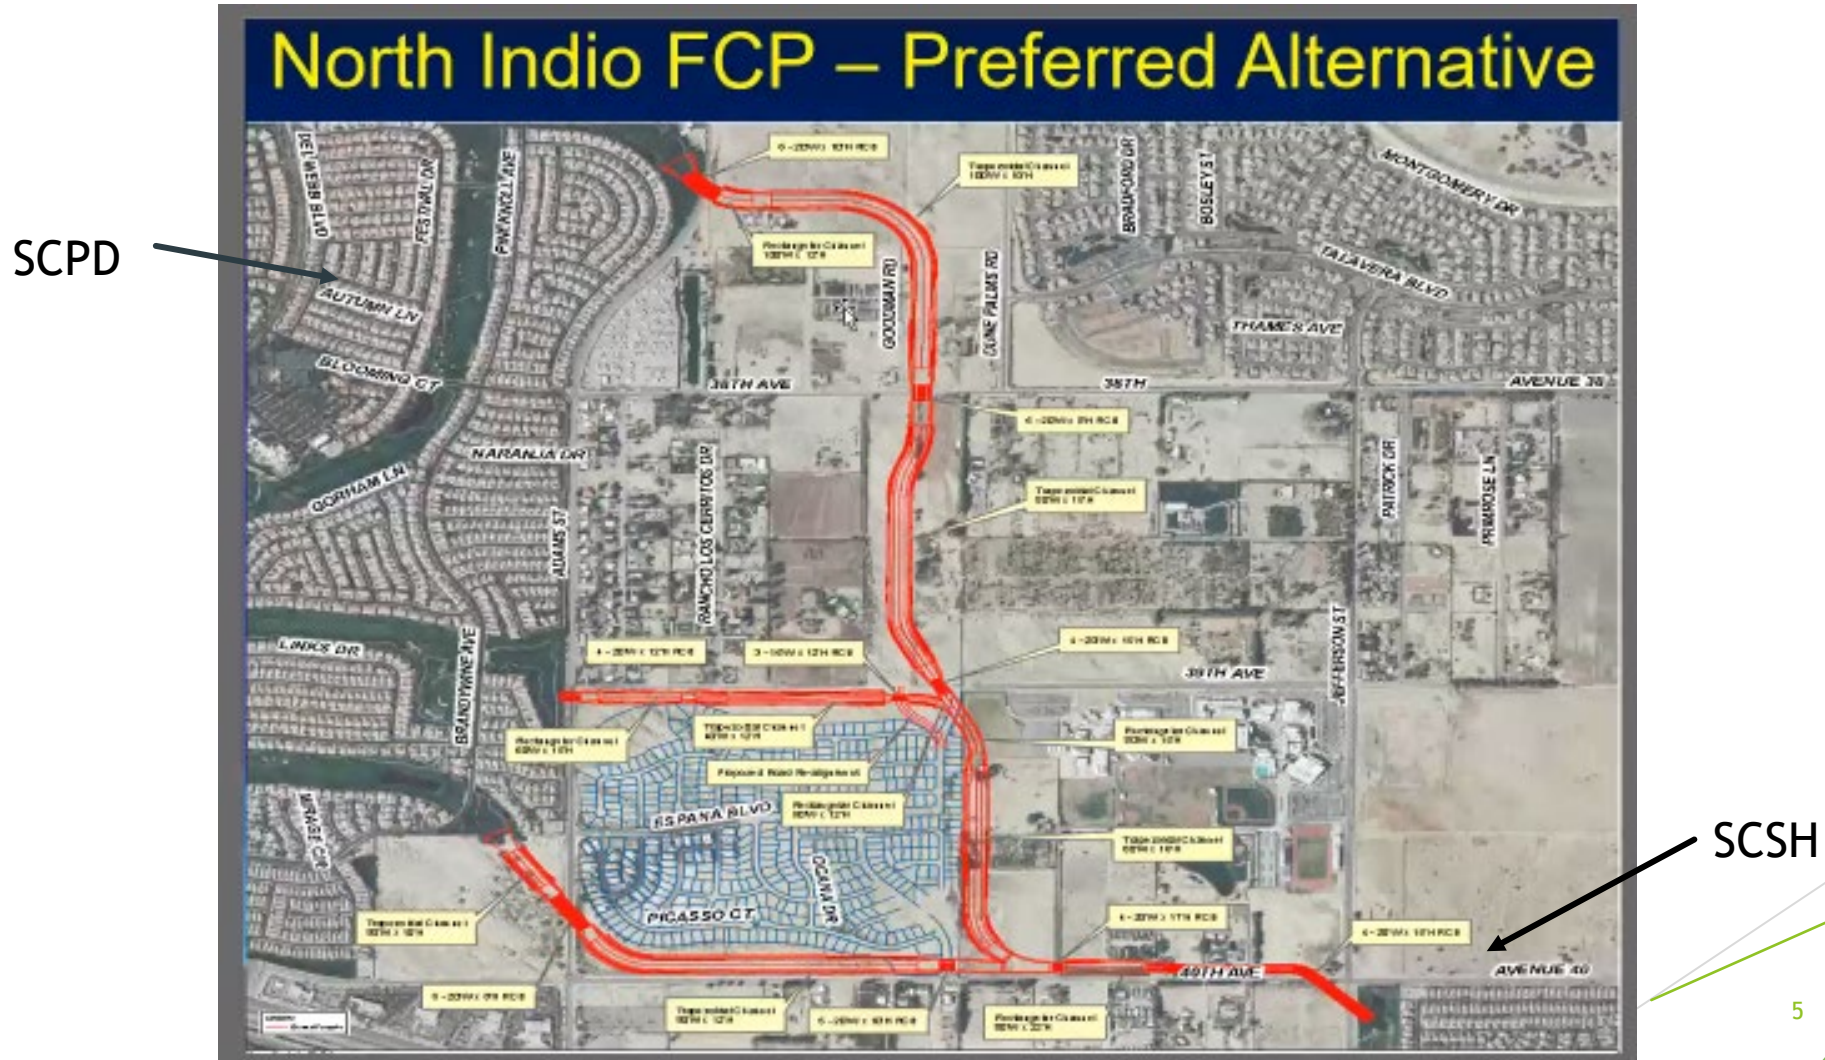

# SCSH Flood Control Project Update



# SCSH North Channel Flood Control Project Update

## Schedule of activities:

### Initial site preparation

Clearing and grubbing	2/25 - 3/10
Videos of adjacent homes	2/25 - 3/1
Dewatering of North Pond	2/25 - 3/10

### Excavation

South pond excavation	3/8 - 3/28
South pond backfill	6/21 - 7/11
North pond excavation	7/12 - 8/1
North pond backfill	10/25 - 11/14

### Slope protection

South slope	3/29 - 6/20
North slope	8/2 - 10/24

### Pier footings and walls

Excavate Footings	10/25 - 7/11
FPS Footings	11/8 - 12/5
FPS Walls 16-Jan-23	12/6 - 1/16/23
FPS Invert	1/17/23 - 2/13/23

# SCSH North Channel Flood Control Project Update

## North Indio Flood Control Pond Construction

Excavate	2/14/23 - 2/27/23
FPS Concrete Pond Liner	2/28/23 - 3/20/23
Finish Grade and Fill Pond	3/21/23 - 4/3/23
Install New Landscape and Irrigation	4/4/23 - 4/24/23



# SCSH North Channel Flood Control Project Update



# SCSH North Channel Flood Control Project Update





# SCSH North Channel Flood Control Project Update



# SCSH North Channel Flood Control Project Update



Channel construction south of  
Ave. 39 crossing looking south



# SCSH North Channel Flood Control Project Update

Questions
